Newcastle C.C. - Building Schools for the Future

KENTON SCHOOL

Summary Asbestos Programme - Indicating Effects On Other Work Phases

Sir Robert McALPINE

Line	Name	Start	Duration	End
1	**School Holidays/ Closure Periods**	**26/05/2009**	**11w**	**26/02/2010**
2	**Asbesto Removal**	**18/05/2009**	**13w 4d**	**21/08/2009**
3	South Block	18/05/2009	4w 4d	19/06/2009
4	West Block	18/05/2009	5w 4d	26/06/2009
5	Central Block	18/05/2009	13w 4d	21/08/2009
6	**Demolition**	**18/05/2009**	**16w 3d**	**11/09/2009**
7	North Block	18/05/2009	4w 4d	19/06/2009
8	South Block	22/06/2009	5w	24/07/2009
9	West Block	29/06/2009	4w	24/07/2009
10	Central Block	08/06/2009	13w 4d	11/09/2009
11	**Phase 3C MUGA Area**	**18/05/2009**	**30w 3d**	**31/12/2009**
12	Retaining Wall	18/05/2009	6w 4d	03/07/2009
13	Fill to MUGA	07/09/2009	3w	25/09/2009
14	MUGA Construction	28/09/2009	9w	27/11/2009
15	Landscaping	30/11/2009	4w 2d	31/12/2009
16	**Phase 4B (Commence After Demolition of South Block)**	**27/07/2009**	**12w 2d**	**31/12/2009**
17	**Phase 3B (Some Works Progressing Until Demolition Of Central & West Block Complete)**	**18/05/2009**	**24w 2d**	**31/12/2009**
18	**All Weather Pitch (Commences After Handover of 4B)**	**04/01/2010**		**04/01/2010**
	North Block Refurbishment (to be confirmed)			
	Final Reinstatement (to be confirmed)			

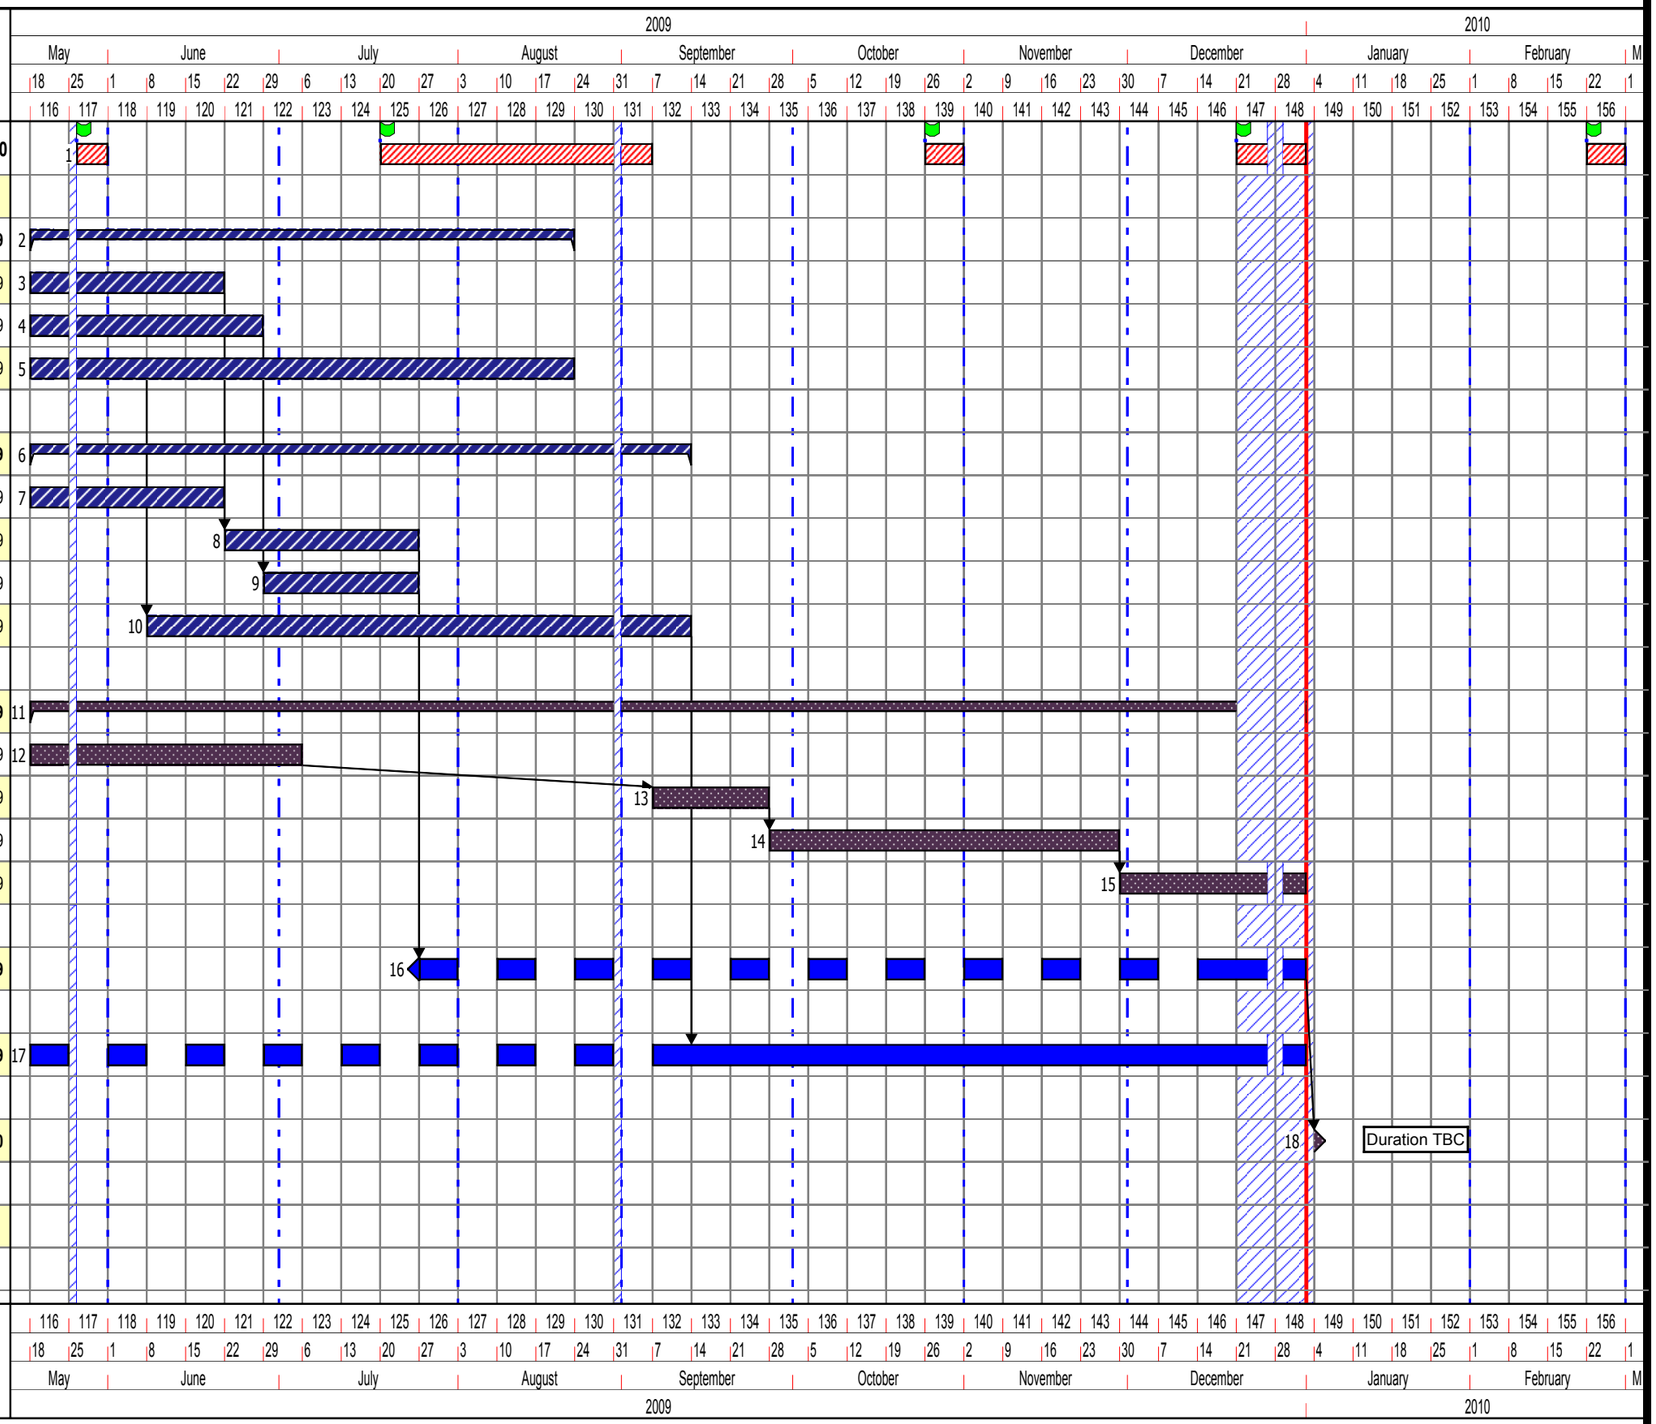

Legend

School Holidays | Demolition | External Works | Construction

Prog. No. McA/N/91574/	Rev. No.	Issue Date: 04/06/2009	Rev. Date : 04/06/2009	Drawn by: Neil Traill	Notes: Issued For Information Only

Project Ref. C:\Documents and Settings\campbell\Kenton School Summary Asbestos Programme.pp

Newcastle C.C. - Building Schools for the Future

KENTON SCHOOL

Summary Asbestos Programme - Indicating Effects On Other Work Phases

Sir Robert McALPINE

Line	Name	Start	Duration	End
1	**School Holidays/ Closure Periods**	**26/05/2009**	**11w**	**26/02/2010**
2	**Asbesto Removal**	**18/05/2009**	**13w 4d**	**21/08/2009**
3	South Block	18/05/2009	4w 4d	19/06/2009
4	West Block	18/05/2009	5w 4d	26/06/2009
5	Central Block	18/05/2009	13w 4d	21/08/2009
6	**Demolition**	**18/05/2009**	**16w 3d**	**11/09/2009**
7	North Block	18/05/2009	4w 4d	19/06/2009
8	South Block	22/06/2009	5w	24/07/2009
9	West Block	29/06/2009	4w	24/07/2009
10	Central Block	08/06/2009	13w 4d	11/09/2009
11	**Phase 3C MUGA Area**	**18/05/2009**	**30w 3d**	**31/12/2009**
12	Retaining Wall	18/05/2009	6w 4d	03/07/2009
13	Fill to MUGA	07/09/2009	3w	25/09/2009
14	MUGA Construction	28/09/2009	9w	27/11/2009
15	Landscaping	30/11/2009	4w 2d	31/12/2009
16	**Phase 4B (Commence After Demolition of South Block)**	**27/07/2009**	**12w 2d**	**31/12/2009**
17	**Phase 3B (Some Works Progressing Until Demolition Of Central & West Block Complete)**	**18/05/2009**	**24w 2d**	**31/12/2009**
18	**All Weather Pitch (Commences After Handover of 4B)**	**04/01/2010**		**04/01/2010**
	North Block Refurbishment (to be confirmed)			
	Final Reinstatement (to be confirmed)			

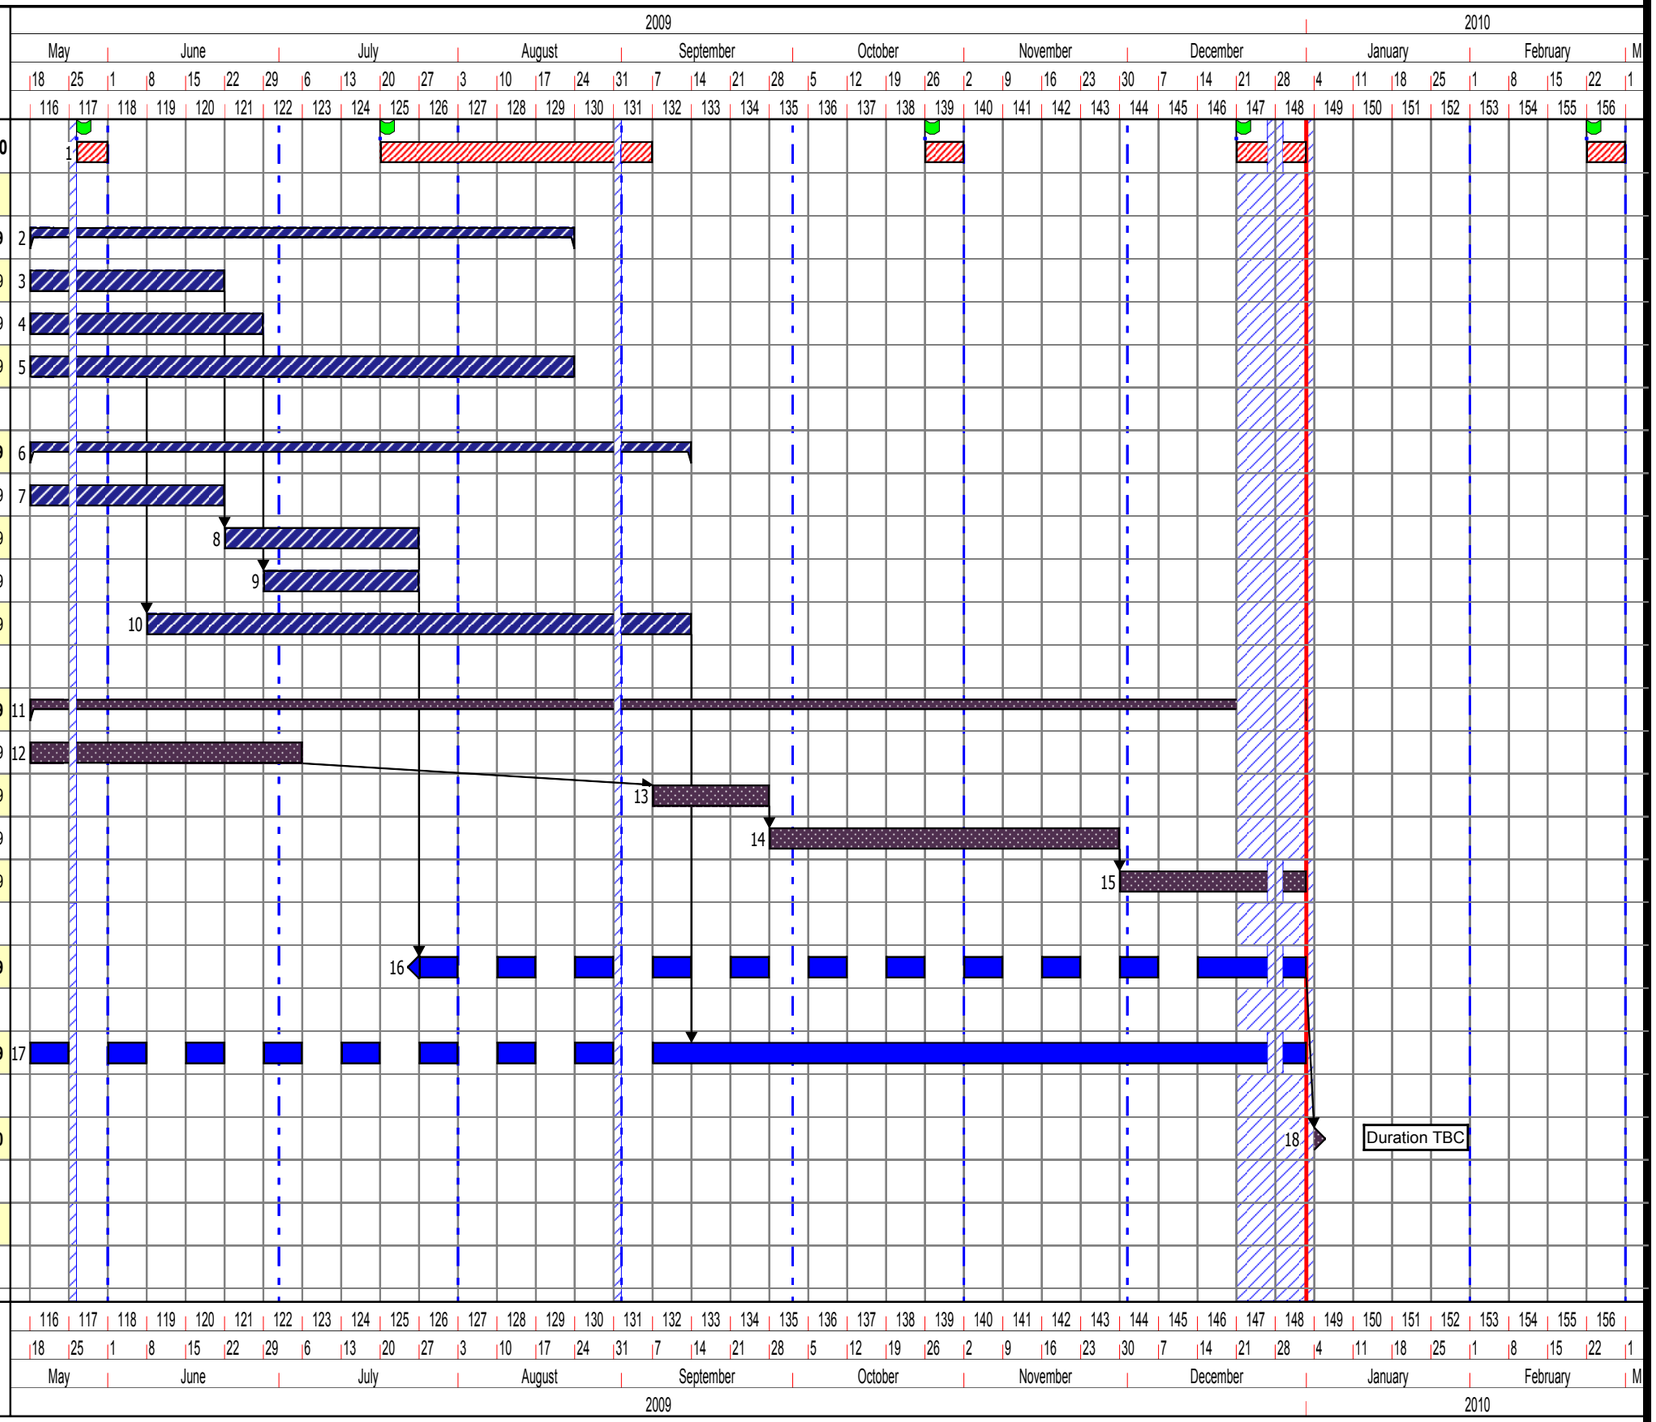

Legend

School Holidays | Demolition | External Works | Construction

Prog. No. McA/N/91574/	Rev. No.	Issue Date: 04/06/2009	Rev. Date : 04/06/2009	Drawn by: Neil Traill	Notes: Issued For Information Only

Project Ref. C:\Documents and Settings\campbell\Kenton School Summary Asbestos Programme.pp
